



7500 W 160th St., Stilwell, KS 66085 • (855) 714- FIRE (3473) • www.firedoorsolutions.com


Firestopping Report Summary

Summary

Open Issues	130
Closed Issues	179
Facility Issues	27



1 RESOLVED

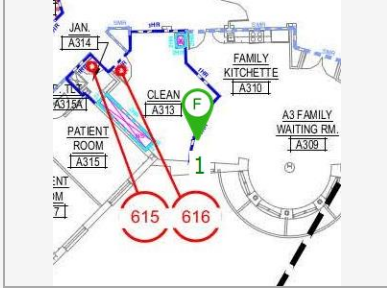Building: Main
Floor: 3




Status: Closed
Description: 2"x4" Scab patch. Needs to be removed. Scab patch is complete.

Before:
After:



2 RESOLVED

Building: Main
Floor: 3

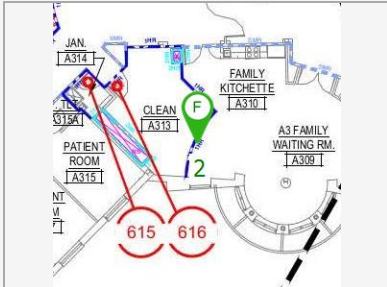


Status: Closed
Description: 1" Open hole. Unsealed

Before:
After:



3 RESOLVED

Building: Main
Floor: 3



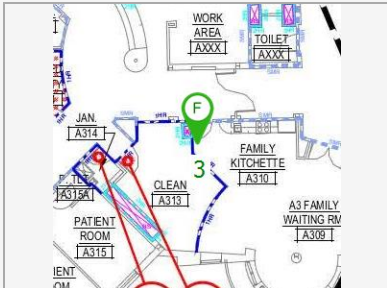

Status: Closed
Description: Improperly sealed. Material needs to be removed and fire stopped.




Before:
After:





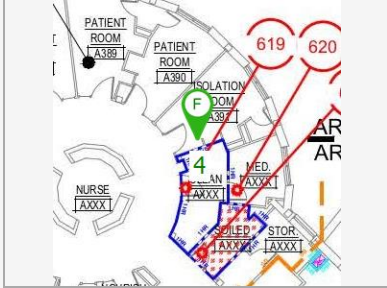




Status: Closed
Description: Mixed materials improperly sealed. Materials have been removed and fire stopped.

Before:
After:


4	RESOLVED	
Building: Main Floor: 3		Status: Closed Description: 3/4" Flex cable. Unsealed
	<div style="display: flex; justify-content: space-around;"> <div style="text-align: center;"> Before:  </div> <div style="text-align: center;"> After:  </div> </div>	

5	RESOLVED	
Building: Main Floor: 3		Status: Closed Description: 3/4" Flexible Conduit. Unsealed
	<div style="display: flex; justify-content: space-around;"> <div style="text-align: center;"> Before:  </div> <div style="text-align: center;"> After:  </div> </div>	

6	NOT RESOLVED	
Building: Main Floor: 3		Status: Open Description: Flexible steel conduit unsealed. Status: Open Description: 1" steel conduit penetrating rated concrete wall assembly. No access due to hard ceiling in bathroom.
	<div style="display: flex; justify-content: space-around;"> <div style="text-align: center;"> Before:  </div> <div style="text-align: center;"> After:  </div> </div>	

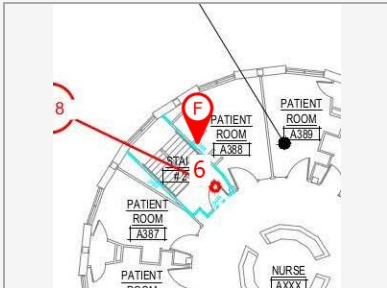
7 NOT RESOLVED

Building: Main
Floor: 3

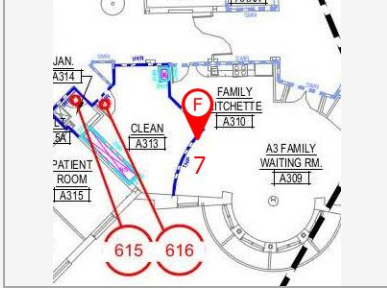


Status: Open
Description: Head of wall. Improperly sealed. Incorrect caulk.

Before:




After:




8 FACILITY ISSUE

Building: Main
Floor: 3




Description: Rated wall does not go to deck.




9 RESOLVED

Building: Main
Floor: 3




Status: Closed
Description: Delete item.

Before:




After:




10 NOT RESOLVED

Building: Main
Floor: 3

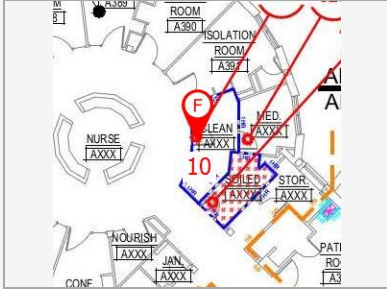


Status: Open
Description: Scab patch needs to be removed and wall repaired around duct.

Before: After:




11 FACILITY ISSUE

Building: Main
Floor: 3




Description: Voids in plaster




12 NOT RESOLVED

Building: Main
Floor: 3

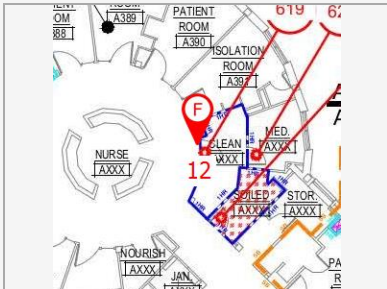

Status: Open
Description: Patch needs to be removed from around duct.


Before: After:




13
NOT RESOLVED


Building: Main

Floor: 3

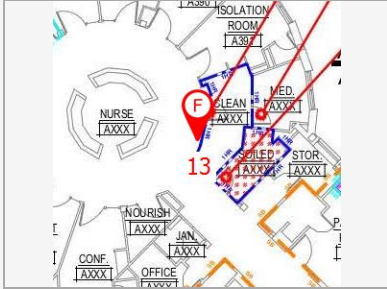

Status: Open
Description: 12"x14" Scab patch needs to be removed. Mixed multi and 3- 1/2" Cooper pipes going through.


Before: 

After: 


14
RESOLVED


Building: Main

Floor: 3

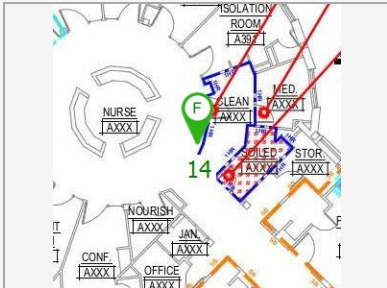

Status: Closed
Description: 1/2" Sleeved cables. Incomplete seal.


Before: 

After: 

15
RESOLVED

Building: Main


Floor: 3





Status: Closed
Description: 2" Metallic pipe. Unsealed


Status: Closed
Description: 3/4" Conduit. Unsealed


Status: Closed
Description: 3/4" Open sleeve. Unsealed


Before: 

After: 

Before: 

After: 


Before: 













After: 

16
RESOLVED

Building: Main

Floor: 3

	<p>Status: Closed Description: 1/2" Flexible steel conduit improperly sealed. Penetration is complete.</p> <p>Status: Closed Description: Blank hole. Unsealed. Penetration is complete.</p> <p>Status: Closed Description: Blank hole improperly sealed. Penetration is complete.</p> <p>Status: Closed Description: 1" Conduit. Unsealed. Penetration has been completed.</p> <p>Status: Closed Description: Cable sleeve needs to be fire stopped. Penetration has been completed.</p> <p>Status: Closed Description: 1" PVC pipe improperly sealed, remove material apply firestop. Penetration has been completed.</p>
-----------------------------------------------------------------------------------	-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------


Before:	After:
	
	
	
	
	
	


17
FACILITY ISSUE

Building: Main

Floor: 3

Description: 8" x 26" hole in rated wall needs repair. 1/4"-1/2" drywall with plaster on top. Recessed behind 5/8" drywall.

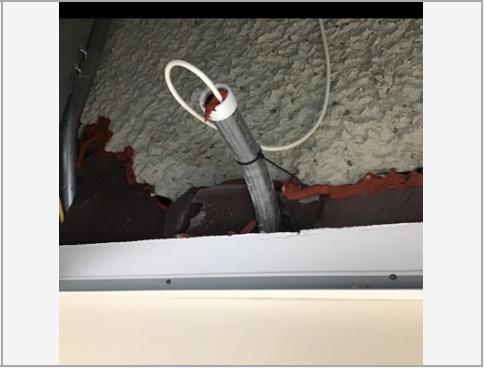




18
NOT RESOLVED

Building: Main


Floor: 3

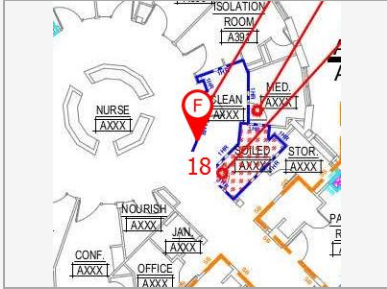


Status: Open

Description: J box cover needed.

Before:




After:



19
NOT RESOLVED

Building: Main


Floor: 3




Status: Open

Description: Head of wall. Improperly sealed. Wrong caulk

Before:




After:



20
RESOLVED

Building: Main


Floor: 3



Status: Closed

Description: 3/4" Conduit. Unsealed

Before:



After:

